



City of Redlands: Municipal Utilities & Engineering Department
35 Cajon Street, Suite 15A, Redlands, CA 92373
(909) 798-7698

ORANGE BLOSSOM TRAIL PHASE 4 PROJECT


Project Engineer: Gerard Nepomuceno
Phone: (909) 798-7584 x4
Email: gnepomuceno@cityofredlands.org

City Inspector: Chris Mergener
Phone: (909) 253-8698 (Cell)
Email: cmergener@cityofredlands.org

PROJECT DETAILS

Contractor: Tryco General Engineering
Description: This project will involve construction of approximately 1 mile of asphalt pavement multi-use path along the Mission Channel. The scope of work also includes installation of drainage structures, concrete work, signs, PVC fencing, and pavement striping.
Start Date: 07/28/25
Anticipated End Date: March 2026
Work Schedule: M-F (7AM - 4PM) excluding city recognized holidays.

CONSTRUCTION PROGRESS

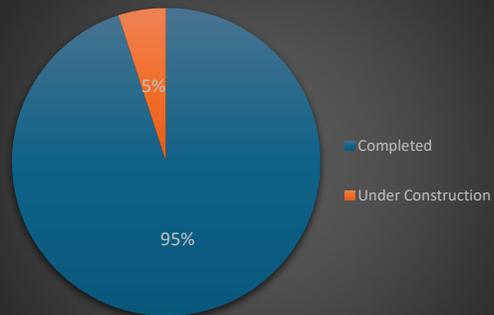

Project Updates & Issues

Contractor is completing punch list items as directed while waiting for material delivery.

2-Week Look Ahead

Contractor will continue with finishing the trailhead monument and completing trail striping. With the current material lead times, only minimal work activities are anticipated on site during February.

Current Construction Process

Construction notices have been given to affected residents. Access to the Orange Blossom Trail from Redlands Boulevard to the I-10 is currently closed until construction is complete.



BUDGET TRACKING

Project Cost:	\$	960,145.00
Approved Change Orders	\$	-
Total Contract Value	\$	960,145.00
Expended to Date:	\$	649,608.00
Balance:	\$	310,537.00

ADDITIONAL INFORMATION

Register online to receive weekly updates by sending an email with the subject line: OBT4 Project Updates. To:
MUEDProjectUpdate@cityofredlands.org

CITY CAPITAL IMPROVEMENT PROJECTS LINK:

<https://www.cityofredlands.org/node/3710>



City of Redlands
Orange Blossom Trail Phase 4
Location Map

Legend

- Proposed Multi-use Path
- Under Construction
- Completed

