



City of Redlands: Municipal Utilities & Engineering Department
 35 Cajon Street, Suite 15A, Redlands, CA 92373
 (909) 798-7698

ORANGE BLOSSOM TRAIL PHASE 4 PROJECT


Project Engineer: Gerard Nepomuceno
Phone: (909) 798-7584 x4
Email: gnepomuceno@cityofredlands.org

City Inspector: Chris Mergener
Phone: (909) 253-8698 (Cell)
Email: cmergener@cityofredlands.org

PROJECT DETAILS

Contractor: Tryco General Engineering
Description: This project will involve construction of approximately 1 mile of asphalt pavement multi-use path along the Mission Channel. The scope of work also includes installation of drainage structures, concrete work, signs, PVC fencing, and pavement striping.
Start Date: 07/28/25
Anticipated End Date: March 2026
Work Schedule: M-F (7AM - 4PM) excluding city recognized holidays.

CONSTRUCTION PROGRESS

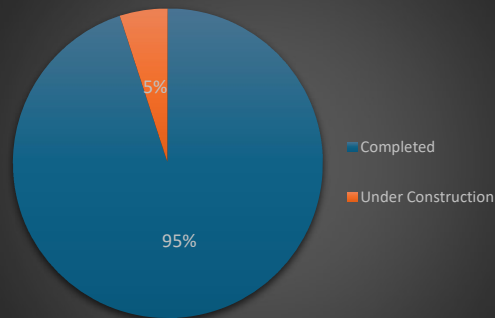

Project Updates & Issues

The contractor is completing corrective work as directed by the City while awaiting delivery of materials needed to proceed with the next phase of work.

2-Week Look Ahead

The contractor will continue completing the trailhead monument and finalizing trail striping. Due to current material lead times, only minimal on-site work activities are anticipated during March.

Current Construction Process

Construction notices have been given to affected residents. Access to the Orange Blossom Trail from Redlands Boulevard to the I-10 is currently closed until construction is complete.



BUDGET TRACKING

Project Cost:	\$	960,145.00
Approved Change Orders	\$	-
Total Contract Value	\$	960,145.00
Expended to Date:	\$	649,608.00
Balance:	\$	310,537.00

ADDITIONAL INFORMATION

Register online to receive weekly updates by sending an email with the subject line: OBT4 Project Updates. To:
MUEDProjectUpdate@cityofredlands.org

CITY CAPITAL IMPROVEMENT PROJECTS LINK:

<https://www.cityofredlands.org/node/3710>



City of Redlands
Orange Blossom Trail Phase 4
Location Map

Legend

- Proposed Multi-use Path
- Under Construction
- Completed

