



City of Redlands: Municipal Utilities & Engineering Department
35 Cajon Street, Suite 15A, Redlands, CA 92373
(909) 798-7698

2025 CIP SEWER PIPELINE REPLACEMENT PROJECT


Project Engineer: Bryan Arellano
Phone: (909) 798-7584 x8
Email: barellano@cityofredlands.org

City Inspector: Chris Mergener
Phone: (909)253-8698 (Cell)
Email: cmergener@cityofredlands.org

PROJECT DETAILS

Contractor: TRYCO GENERAL ENGINEERING
Description: This project will involve rehabilitating approximately 8,000 linear feet of sewer pipeline and the removal and replacement of various manholes.
Start Date: 11/3/25
Anticipated End Date: April 2026
Work Schedule: M-F (7AM - 4PM) excluding city recognized holidays.

CONSTRUCTION PROGRESS

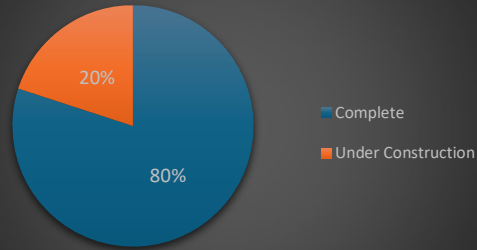

Project Updates & Issues

Tryco's crew has begun the removal and replacement of the sewer pipeline on Dreka Alley between Ohio Street and Webster Street. The crew also continues work on Washington Street, including backfilling the sewer main, connecting laterals, and completing the removal and replacement of a manhole.

2-Week Look Ahead

The crew will continue sewer replacement work on Dreka Alley and finish compaction of the sewer main and installation of the manhole on Washington Street.

Current Construction Process

Construction notices have been given to affected residents. If restricted parking is necessary, "No Parking" signs will be posted 48 hours in advance of construction activities.



Crew backfilling the sewer main trench on Washington Street.

BUDGET TRACKING


Project Cost:	\$	1,494,516.00
Approved Change Orders	\$	-
Total Contract Value	\$	1,494,516.00
Expended to Date:	\$	616,082.51
Balance:	\$	878,433.49

ADDITIONAL INFORMATION

Register online to receive weekly updates by sending an email with the subject line: **2025 CIP Sewer Project Updates**. To:
MUEDProjectUpdate@cityofredlands.org

INTERACTIVE CITY CAPITAL IMPROVEMENT PROJECT MAP LINK:

<https://www.cityofredlands.org/node/3710>

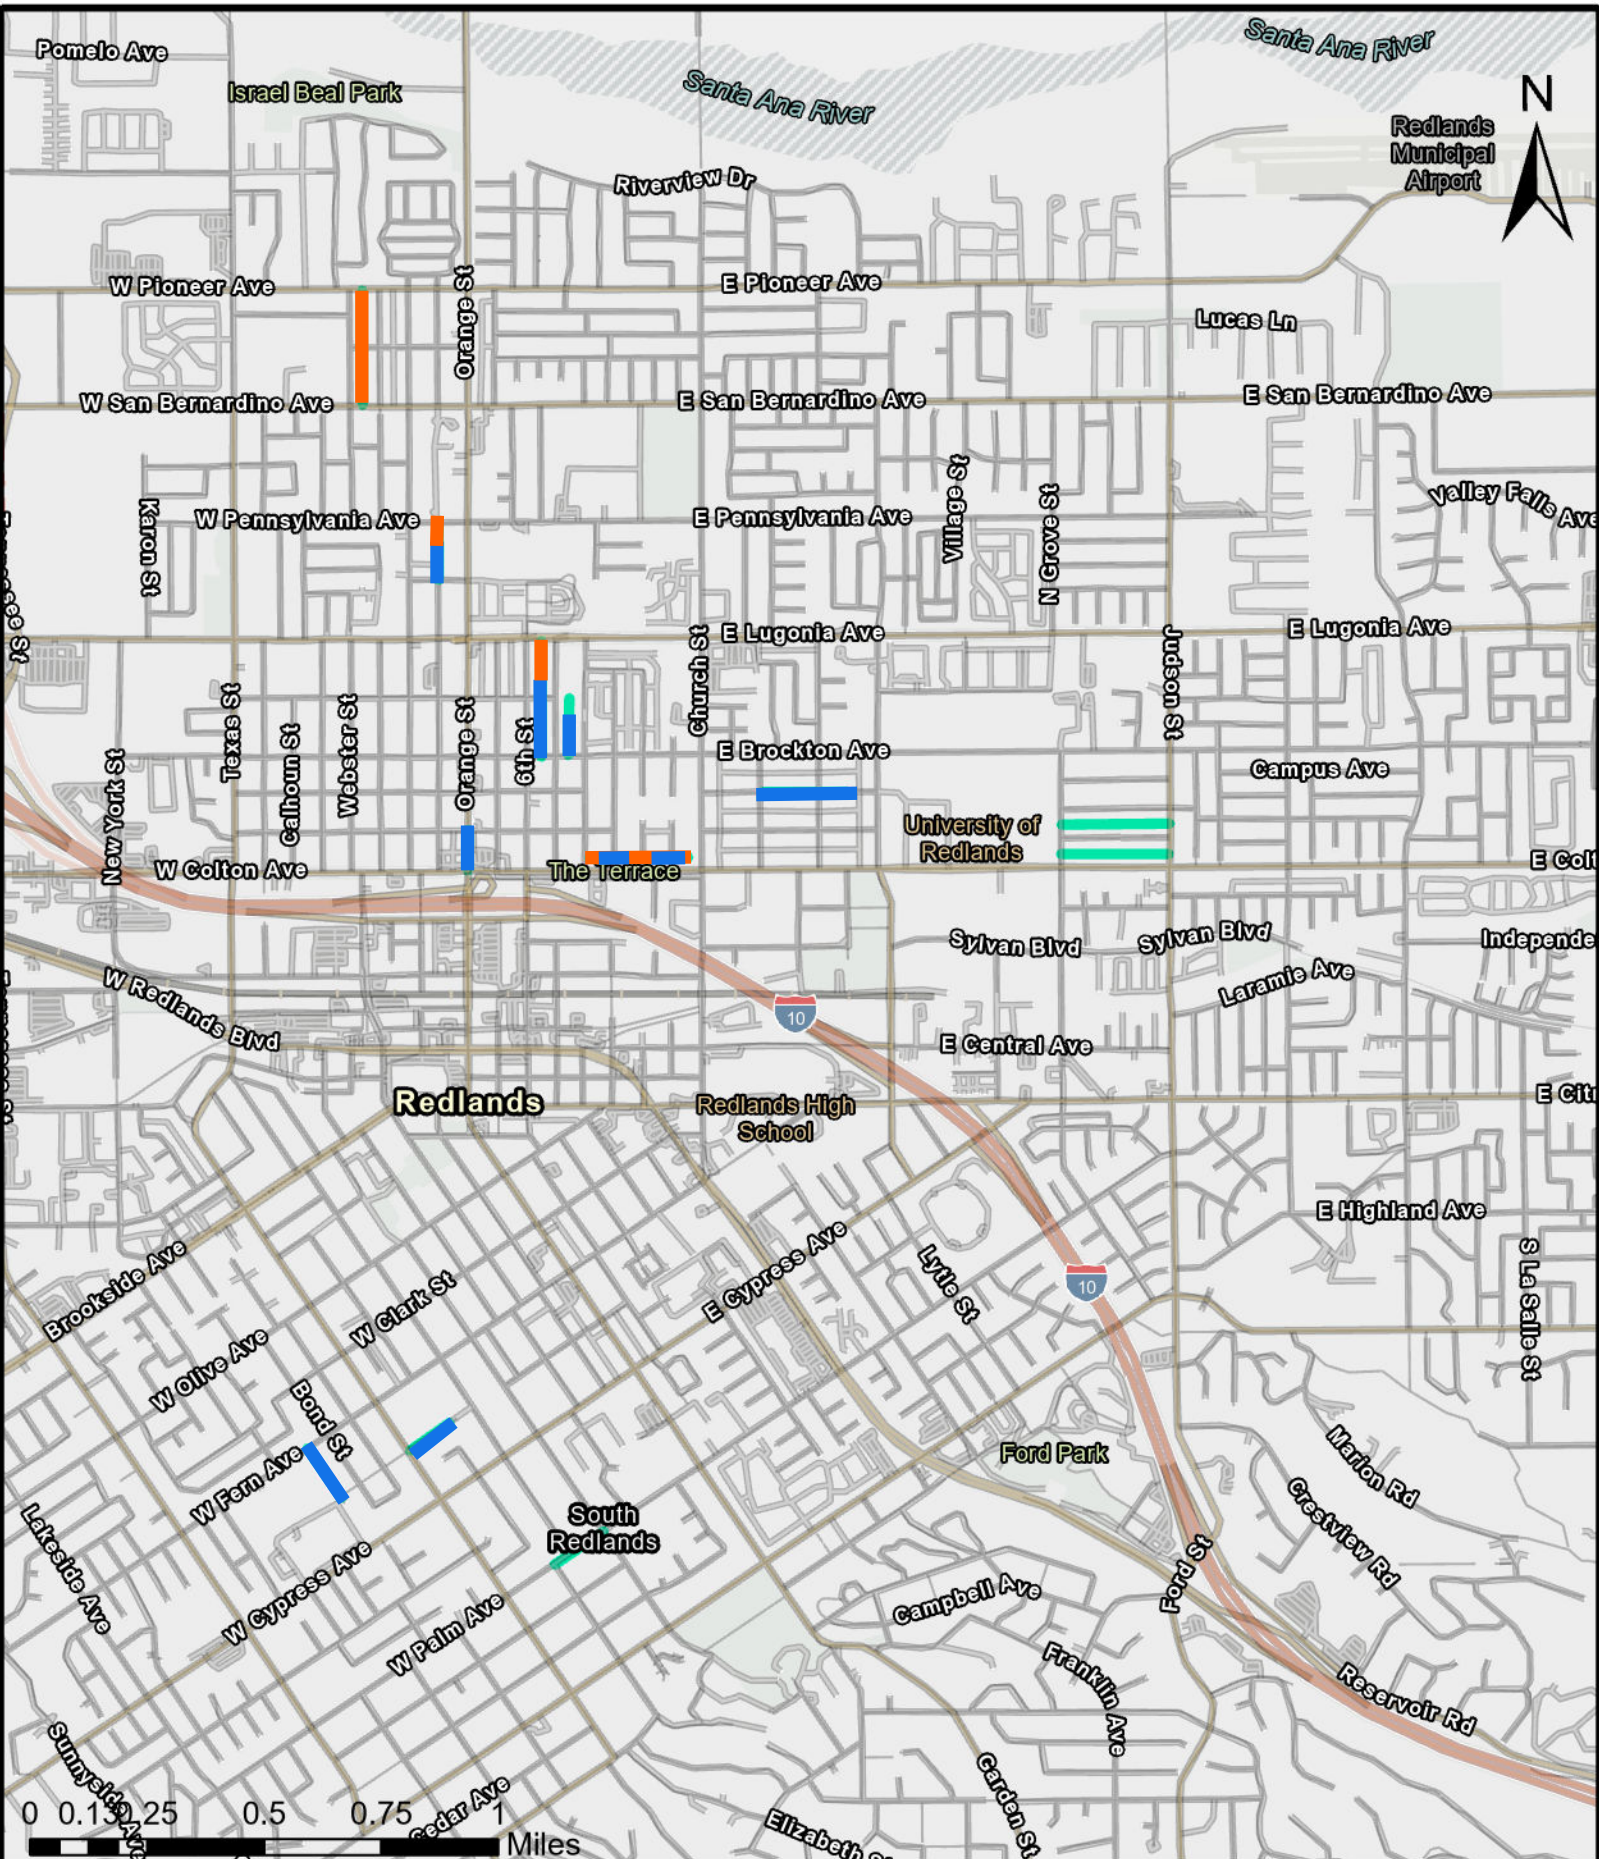

2025 CIP SEWER PIPELINE REPLACEMENT PROJECT LOCATION MAP



— Sewer CIP FY 25/26

— -Under Construction
— -Completed
