



**City of Redlands: Municipal Utilities & Engineering Department**  
**35 Cajon Street, Suite 15A, Redlands, CA 92373**  
**(909) 798-7698**

## 2025 CIP SEWER PIPELINE REPLACEMENT PROJECT

**Project Engineer:** Bryan Arellano

**Phone:** (909) 798-7584 x8

**Email:** barellano@cityofredlands.org

**City Inspector:** Chris Mergener

**Phone:** (909)253-8698 (Cell)

**Email:** cmergener@cityofredlands.org

### PROJECT DETAILS

**Contractor:** TRYCO GENERAL ENGINEERING


**Description:** This project will involve rehabilitating approximately 8,000 linear feet of sewer pipeline and the removal and replacement of various manholes.

**Start Date:** 11/3/25

**Anticipated End Date:** April 2026

**Work Schedule:** M-F (7AM - 4PM) excluding city recognized holidays.

### CONSTRUCTION PROGRESS

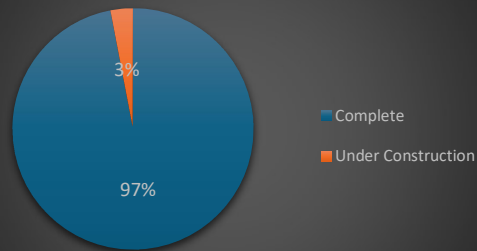

### Project Updates & Issues

The subcontractor has completed all Cured-In-Place Pipe (CIPP) installations per the plans. Tryco will proceed with the final section of removal and replacement along the alley between East Western Avenue and East Brockton Avenue.

### 2-Week Look Ahead

Tryco is anticipated to complete the final section of sewer replacement near the 6th Street alley.

### Current Construction Process

Construction notices have been given to affected residents. If restricted parking is necessary, "No Parking" signs will be posted 48 hours in advance of construction activities.



Crew installing a new sewer main on Palm Avenue.

### BUDGET TRACKING


Project Cost:	\$	1,494,516.00
Approved Change Orders	\$	-
<b>Total Contract Value</b>	<b>\$</b>	<b>1,494,516.00</b>
Expended to Date:	\$	616,082.51
Balance:	\$	878,433.49

### ADDITIONAL INFORMATION

Register online to receive weekly updates by sending an email with the subject line: **2025 CIP Sewer Project Updates**. To: [MUEDProjectUpdate@cityofredlands.org](mailto:MUEDProjectUpdate@cityofredlands.org)

INTERACTIVE CITY CAPITAL IMPROVEMENT PROJECT MAP LINK:

<https://www.cityofredlands.org/node/3710>

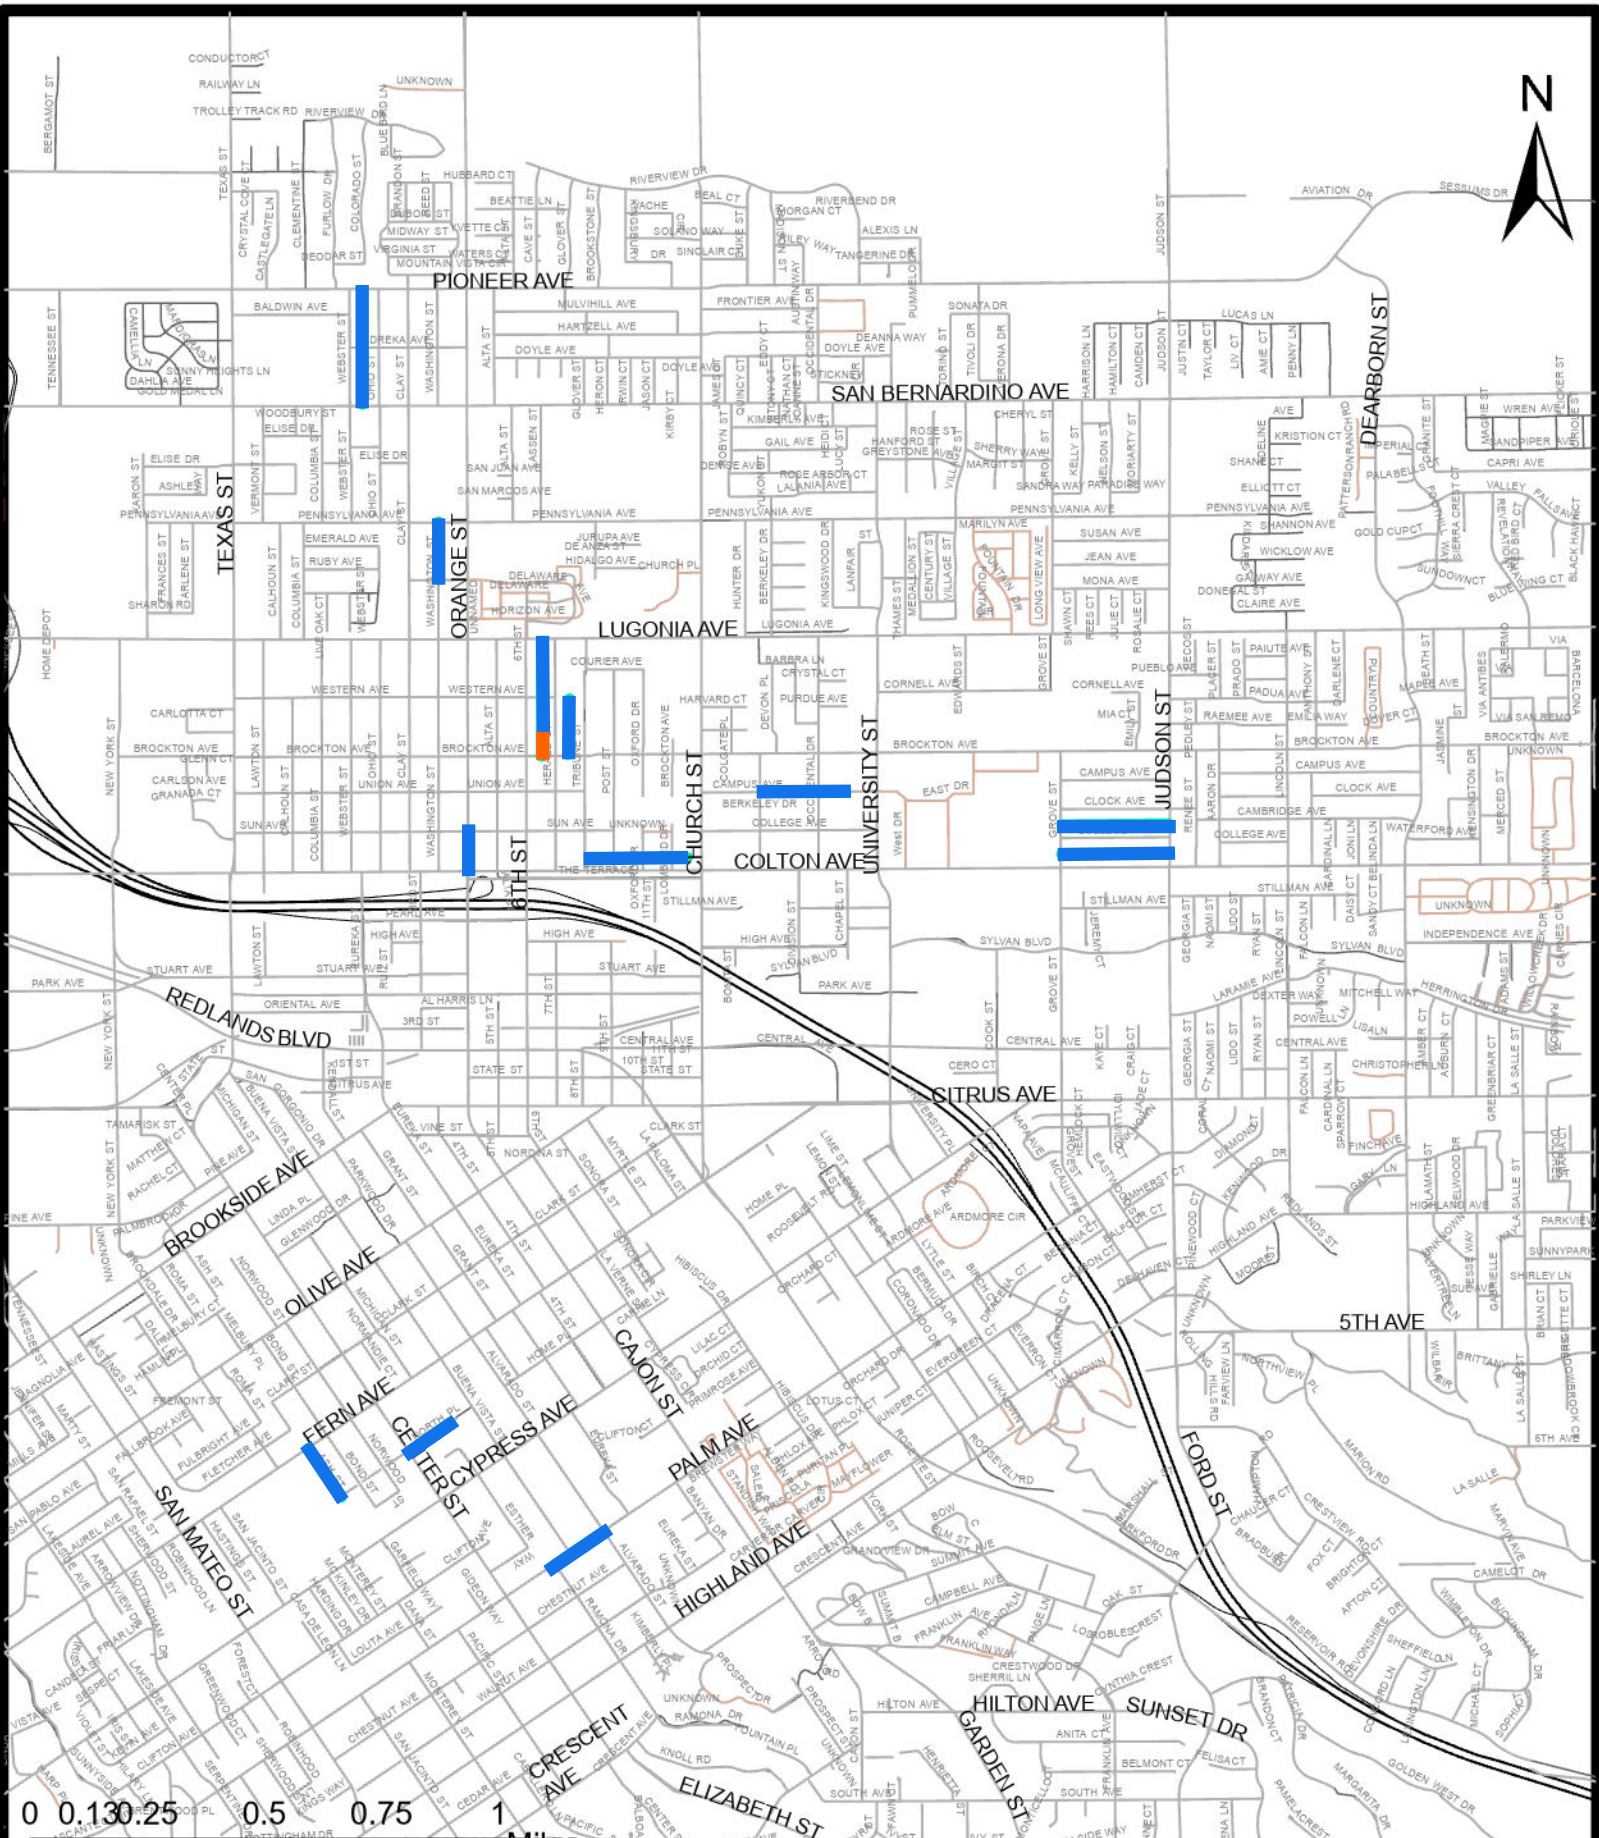

# 2025 CIP SEWER PIPELINE REPLACEMENT PROJECT LOCATION MAP



**Sewer CIP FY 25/26**

- -Under Construction
- -Completed
