



**City of Redlands: Municipal Utilities & Engineering Department**  
**35 Cajon Street, Suite 15A, Redlands, CA 92373**  
**(909) 798-7698**

## 2025 CIP WATER PIPELINE REPLACEMENT PROJECT


**Project Engineer:** Elva Arellanes  
**Phone:** (909) 798-7584 x9  
**Email:** earellanes@cityofredlands.org

**City Inspector:** Daniel Murbarger  
**Phone:** (909) 437-8440 (Cell)  
**Email:** dmurbarger@cityofredlands.org

### PROJECT DETAILS

**Contractor:** MCC Pipeline, Inc.  
**Description:** This project will involve replacing approximately 14,500 linear feet of ductile iron water pipeline ranging from 8 to 24 inches at various locations throughout the City  
**Start Date:** 4/6/26  
**Anticipated End Date:** July 2026  
**Work Schedule:** M-F (7AM - 4PM) excluding city recognized holidays. If necessary, night hours M-F (9PM - 6AM).

### CONSTRUCTION PROGRESS

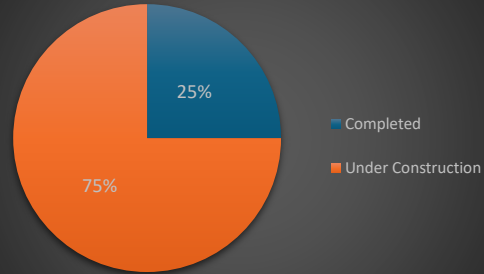

### Project Updates & Issues

The contractor, MCC, is currently onsite on Sunset Hills Ln, continuing excavation and installation of 8-inch ductile iron pipe (DIP). The contractor is also scheduled to perform tie-in work at the intersections of Orange Street and Western Avenue, and Orange Street and Lugonia Avenue. To minimize disruptions to the public, tie-ins are being conducted during nighttime hours, from 9:00 p.m. to 6:00 a.m.

### 2-Week Look Ahead

The contractor will continue installing an 8-inch DIP, water services, and fire hydrants Sunset Hills Ln.

### Current Construction Process

Typically, the replacement of waterlines will take 3-4 weeks from excavation of the trench to connecting to the existing line. Final paving is done when multiple sections of waterline have been replaced. Construction notices have been given to affected residents. For temporary water shutdowns in your area, notices will be given at least 48 hours in advance of construction activities.



**Installing an 8 Inch DIP pipe at Sunset Hills**

### BUDGET TRACKING


Project Cost:	\$	4,003,595.00
Approved Contract Amendment		
Total Contract Value	\$	4,003,595.00
Expended to Date:	\$	508,776.33
Balance:	\$	3,494,818.67


### ADDITIONAL INFORMATION

Register online to receive weekly updates by sending an email with the subject line: CIP Water Project Updates. To:  
[MUEDProjectUpdate@cityofredlands.org](mailto:MUEDProjectUpdate@cityofredlands.org)

CITY CAPITAL IMPROVEMENT PROJECT MAP LINK:

<https://experience.arcgis.com/experience/1c6063e0f303451d88a88727b7cfa77d>

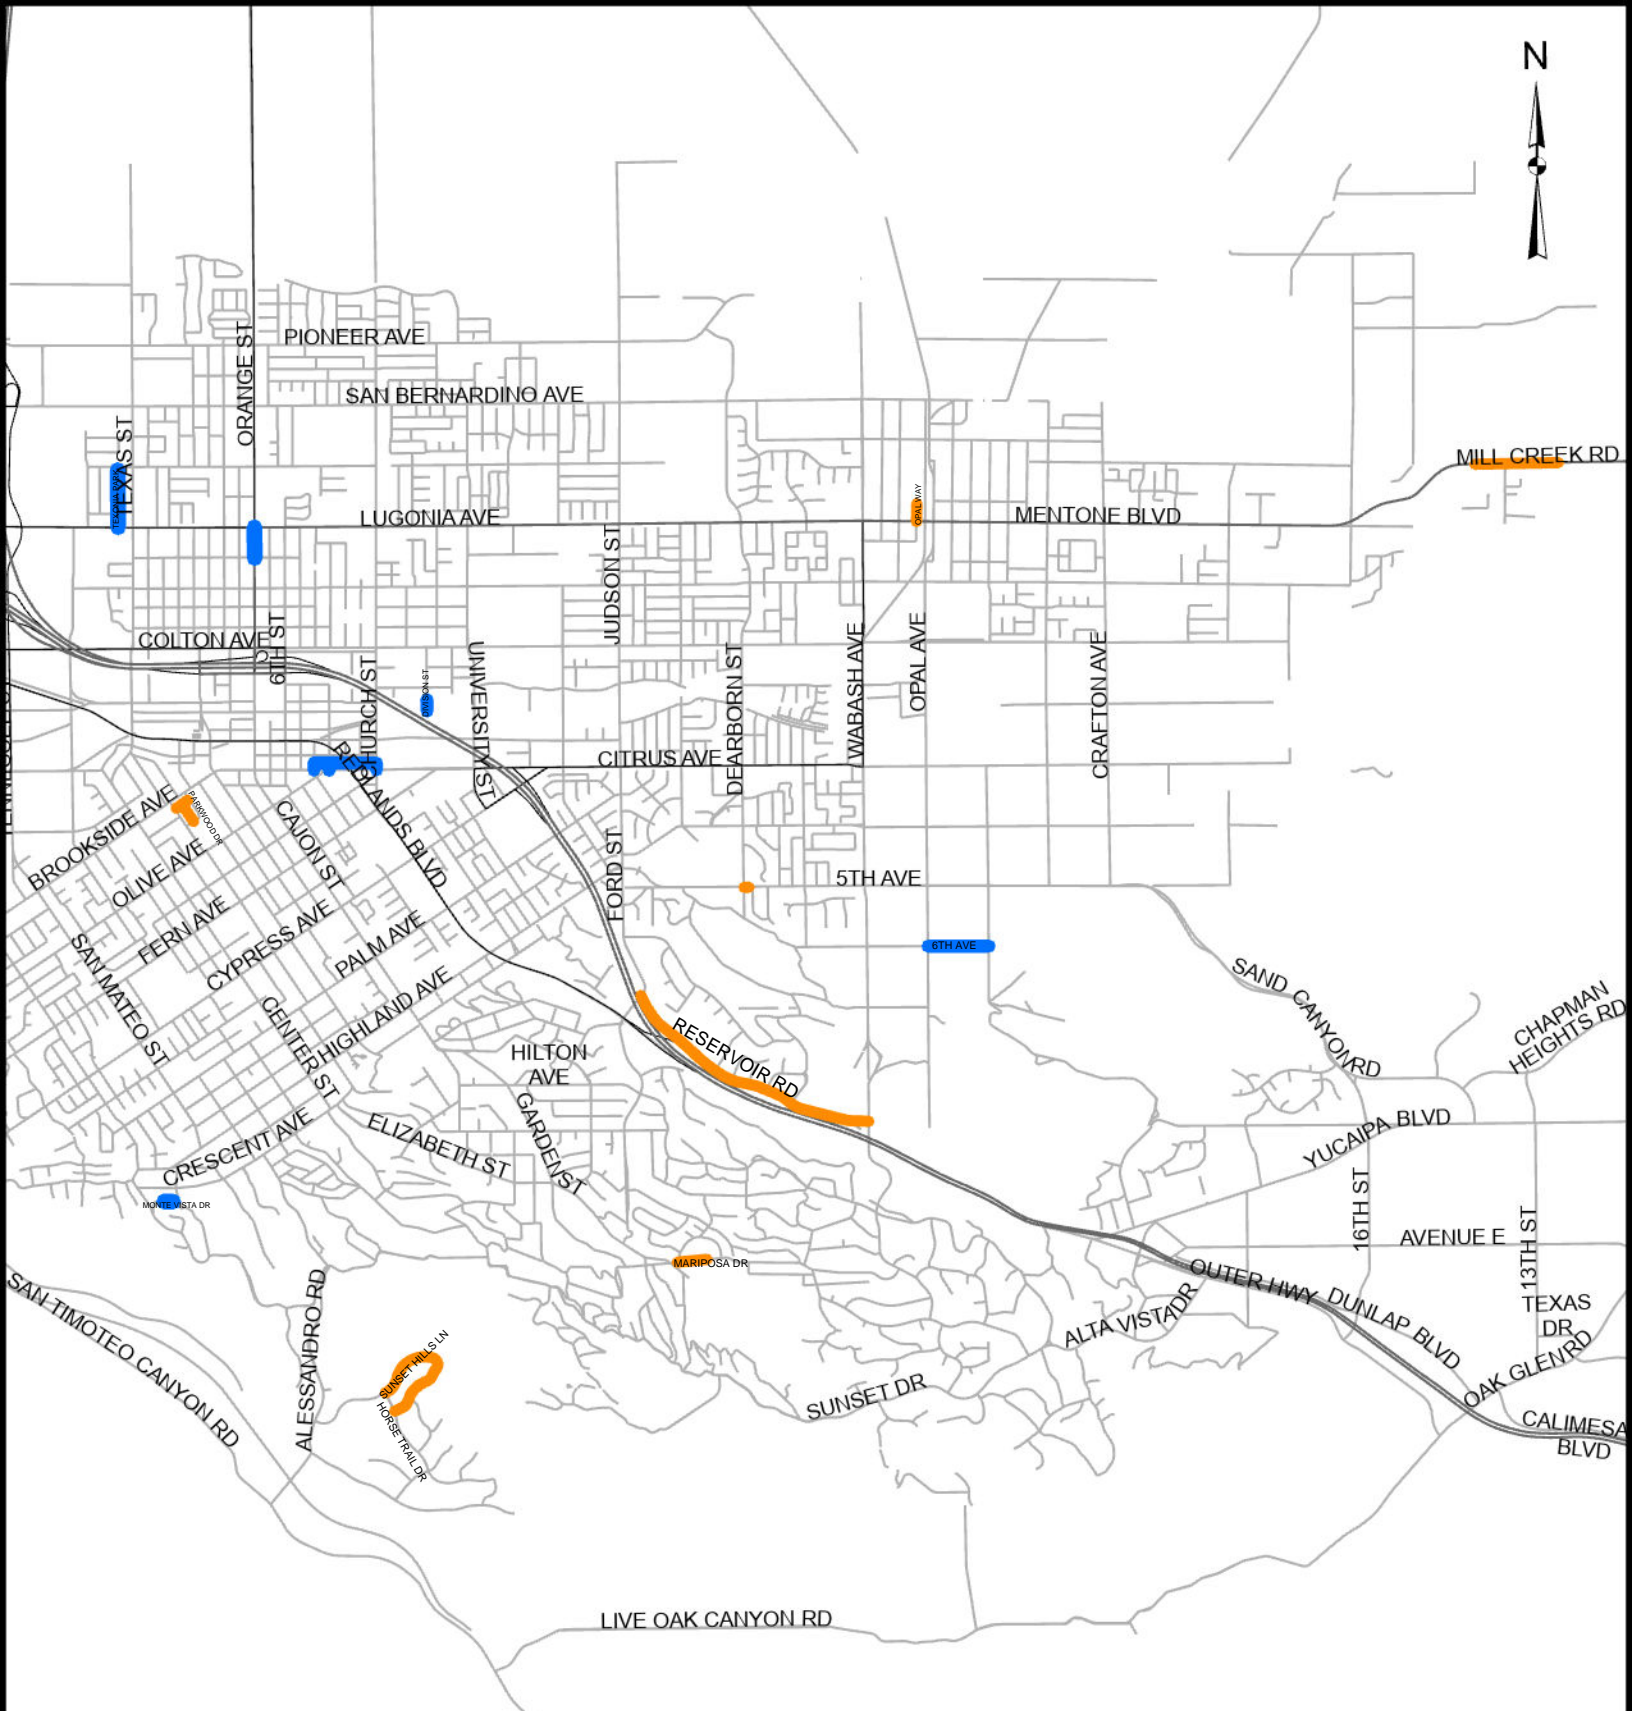

-  Completed
-  Under Construction



# 2025 CIP Water Pipeline Replacement Project Location Map
