



**City of Redlands: Municipal Utilities & Engineering Department**  
**35 Cajon Street, Suite 15A, Redlands, CA 92373**  
**(909) 798-7698**

## 2025 CIP WATER PIPELINE REPLACEMENT PROJECT


**Project Engineer:** Elva Arellanes  
**Phone:** (909) 798-7584 x9  
**Email:** earellanes@cityofredlands.org

**City Inspector:** Daniel Murbarger  
**Phone:** (909) 437-8440 (Cell)  
**Email:** dmurbarger@cityofredlands.org

### PROJECT DETAILS

**Contractor:** MCC Pipeline, Inc.  
**Description:** This project will involve replacing approximately 14,500 linear feet of ductile iron water pipeline ranging from 8 to 24 inches at various locations throughout the City  
**Start Date:** 4/6/26  
**Anticipated End Date:** July 2026  
**Work Schedule:** M-F (7AM - 4PM) excluding city recognized holidays. If necessary, night hours M-F (9PM - 6AM).

### CONSTRUCTION PROGRESS

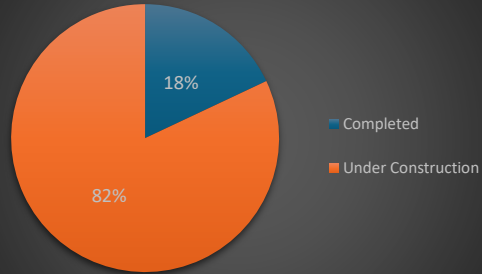

### Project Updates & Issues

**Contractor MCC completed scheduled night work on Orange St./Highway 38. Due to existing wooden railroad ties encountered in the trench, the crew only completed installation of one long-side and one short-side 1-inch copper service. MCC also began installation of a 12-inch non-potable pipe at Texonia Park and completed tie-in work on Division Street.**

### 2-Week Look Ahead

The contractor will continue with the installation of a 12-inch non-potable pipe in Texonia Park. They will conduct a pressure test on Orange Street and finish the tie-in connections on 6th Avenue and Monte Vista Drive. Once these tasks are completed, they will move to Horse Trail Road.

### Current Construction Process

Typically, the replacement of waterlines will take 3-4 weeks from excavation of the trench to connecting to the existing line. Final paving is done when multiple sections of waterline have been replaced. Construction notices have been given to affected residents. For temporary water shutdowns in your area, notices will be given at least 48 hours in advance of construction activities.



**Installing 12" non-potable pipe at Texonia Park**

### BUDGET TRACKING


<i>Project Cost:</i>	\$	4,003,595.00
<i>Approved Contract Amendment</i>		
<i>Total Contract Value</i>	\$	4,003,595.00
<i>Expended to Date:</i>	\$	508,776.33
<i>Balance:</i>	\$	3,494,818.67

### ADDITIONAL INFORMATION

*Register online to receive weekly updates by sending an email with the subject line: CIP Water Project Updates. To:*  
[MUEDProjectUpdate@cityofredlands.org](mailto:MUEDProjectUpdate@cityofredlands.org)

CITY CAPITAL IMPROVEMENT PROJECT MAP LINK:

<https://www.cityofredlands.org/node/3710>

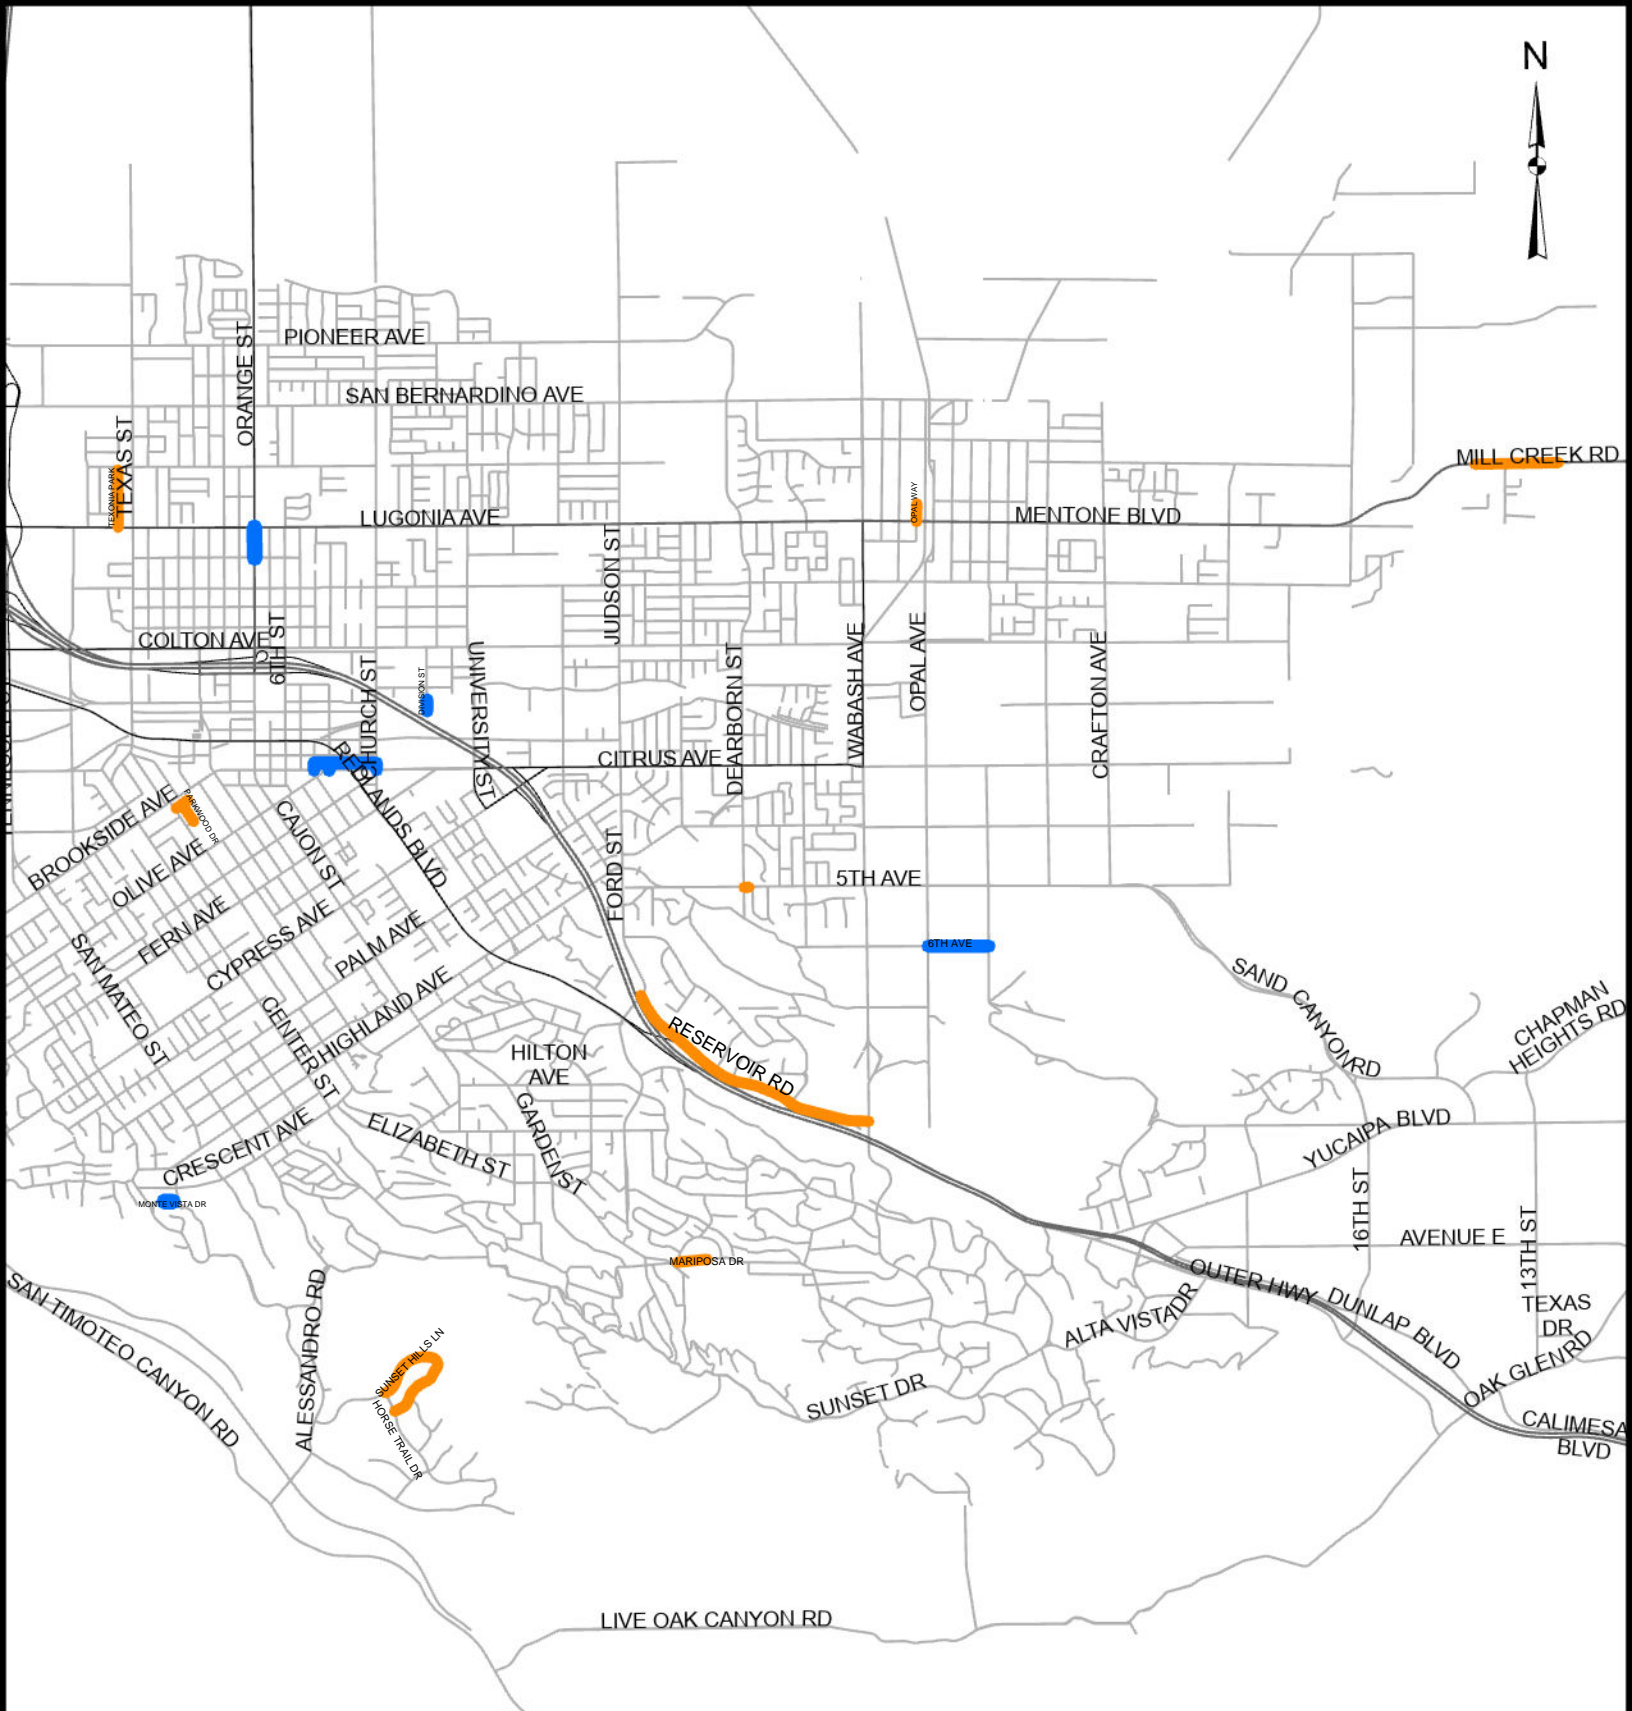

-  Completed
-  Under Construction



# 2025 CIP Water Pipeline Replacement Project Location Map
