



City of Redlands: Municipal Utilities & Engineering Department
35 Cajon Street, Suite 15A, Redlands, CA 92373
(909) 798-7698

2025 CIP WATER PIPELINE REPLACEMENT PROJECT

Project Engineer: Elva Arellanes
Phone: (909) 798-7584 x9
Email: earellanes@cityofredlands.org

City Inspector: Daniel Murbarger
Phone: (909) 437-8440 (Cell)
Email: dmurbarger@cityofredlands.org

PROJECT DETAILS

Contractor: MCC Pipeline, Inc.


Description: This project will involve replacing approximately 14,500 linear feet of ductile iron water pipeline ranging from 8 to 24 inches at various locations throughout the City

Start Date: 4/6/26

Anticipated End Date: August 2026

Work Schedule: M-F (7AM - 4PM) excluding city recognized holidays. If necessary, night hours M-F (9PM - 6AM).

CONSTRUCTION PROGRESS

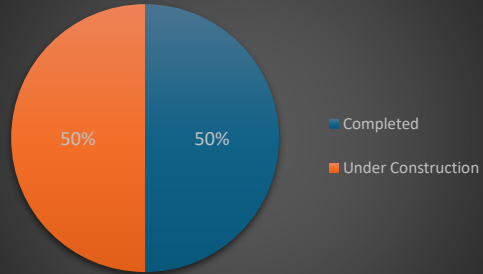

Project Updates & Issues

The contractor, MCC, has completed the installation of water services at Sunset Hills Lane. The contractor is continuing the installation of the 16" DIP at Reservoir Rd.

2-Week Look Ahead

The contractor will complete the installation of the 16" water line at Reservoir Rd, then move to Mariposa Dr. to pressure test, chlorinate the pipeline, and install water services.

Current Construction Process

Typically, the replacement of waterlines will take 3-4 weeks from excavation of the trench to connecting to the existing line. Final paving is done when multiple sections of waterline have been replaced. Construction notices have been given to affected residents. For temporary water shutdowns in your area, notices will be given at least 48 hours in advance of construction activities.



Installing 16-Inch DIP at Reservoir Rd

BUDGET TRACKING



Project Cost:	\$	4,003,595.00
Approved Contract Amendment		
Total Contract Value	\$	4,003,595.00
Expended to Date:	\$	994,802.94
Balance:	\$	3,008,792.06

ADDITIONAL INFORMATION

Register online to receive weekly updates by sending an email with the subject line: **CIP Water Project Updates**. To:
MUEDProjectUpdate@cityofredlands.org

CITY CAPITAL IMPROVEMENT PROJECT MAP LINK:

<https://experience.arcgis.com/experience/1c6063e0f303451d88a88727b7cfa77d>

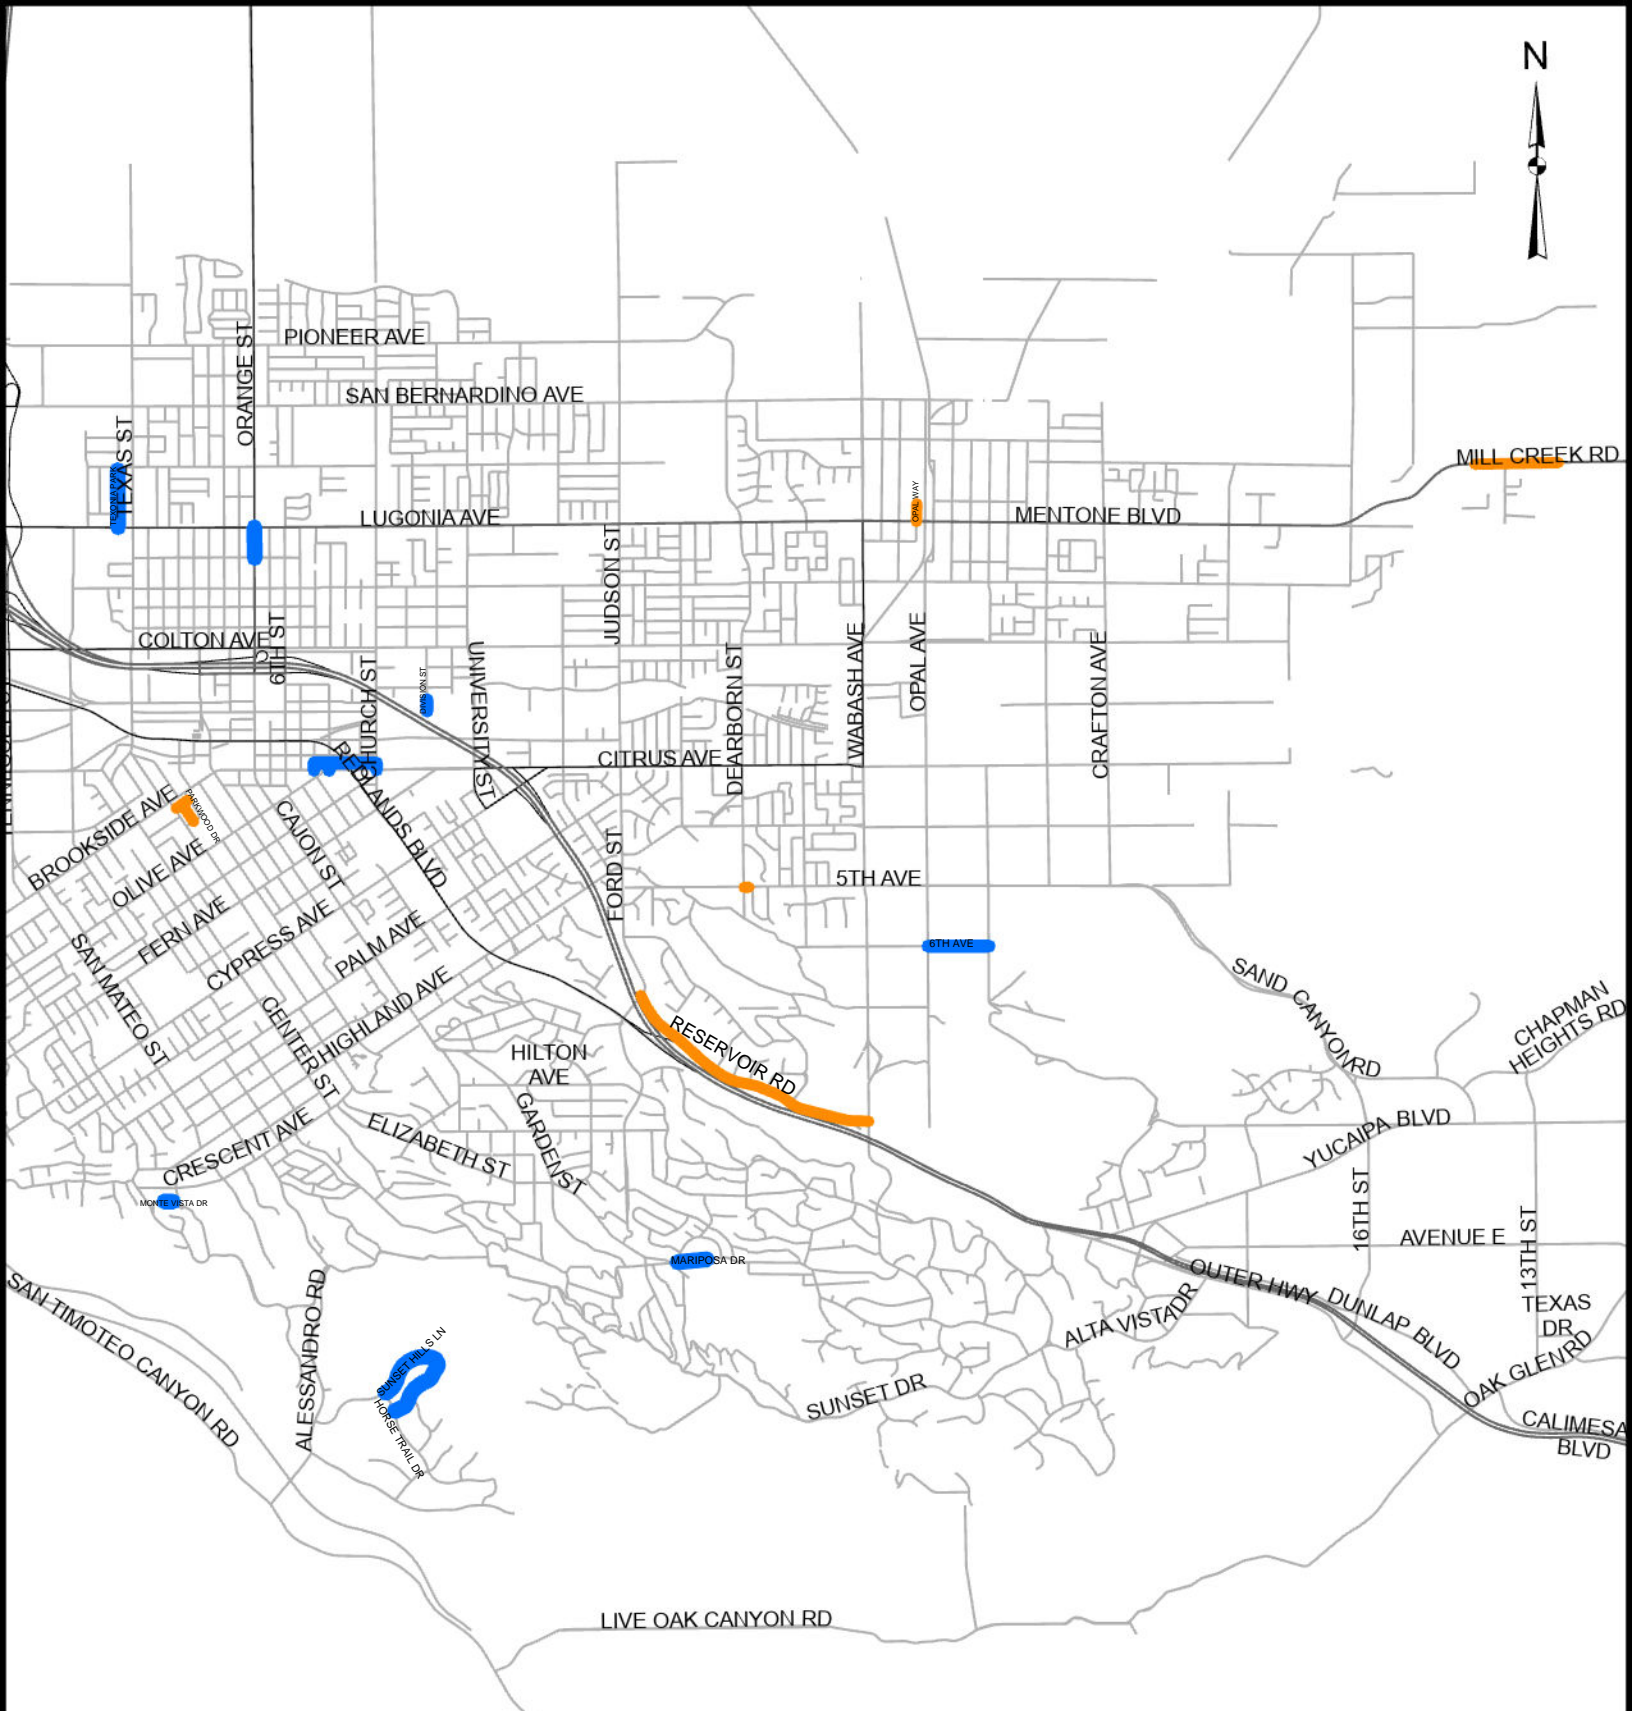

-  Completed
-  Under Construction



2025 CIP Water Pipeline Replacement Project Location Map
